

My Company Name

My Address


To: FRITZ ARCHITECTS LTD.
1220 - 30 STREET N.
SOUTHBRIDGE, DAKOTA
86153

AL FRITZ

Project: MEDICAL BUILDING GEOTECHNICAL

Proctor Report

Project Number: M94-02-5
Report Number: 1
Report Date: 19-Jan-11
Copies To: city,dot
Tested By: prf
Source: ged
Sample Date: 19-Jan-11
Date Received: 19-Jan-11
Date Tested: 19-Jan-11

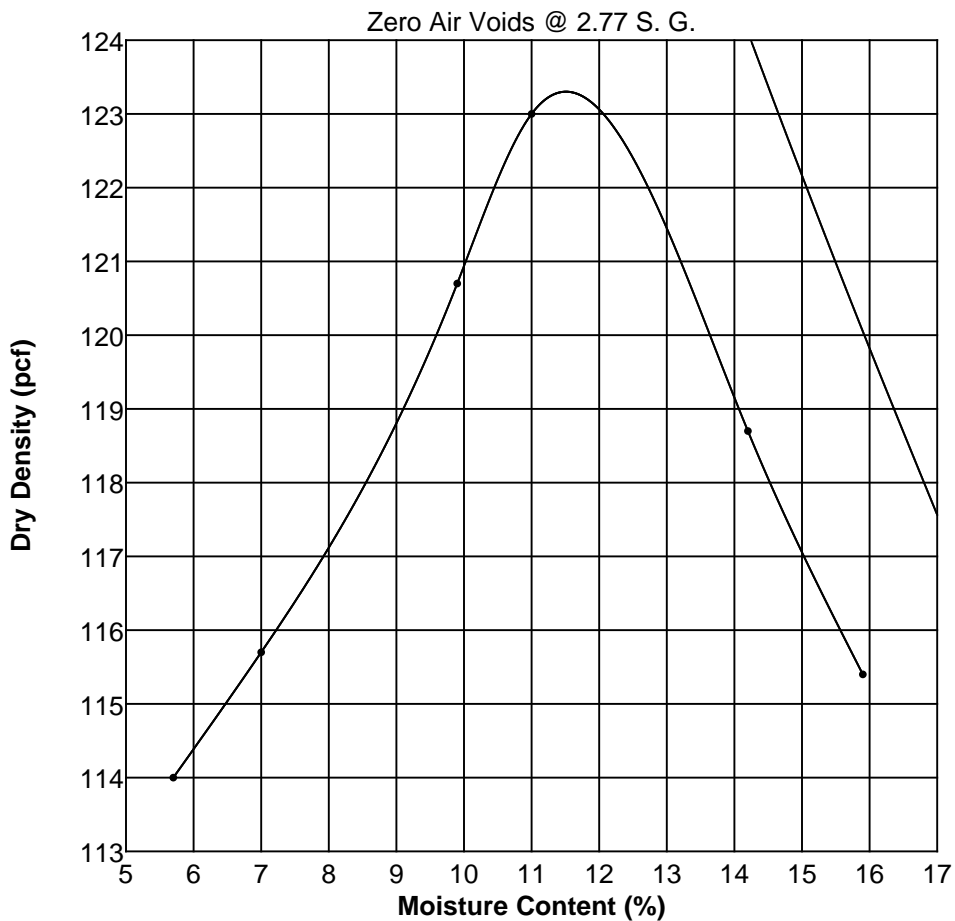

Optimum	Max Dry
Moisture	Density
(%)	(pcf)
11.5	123.3

Optimum	Max Dry
Moisture	Density
(%)	(pcf)
11.5	123.3
10	136.3
20	152.4
30	172.8
40	199.6
50	236.1

Moisture	Dry	Wet
Content	Density	Density
(%)	(pcf)	(pcf)
5.7	114.0	120.5
7.0	115.7	123.8
9.9	120.7	132.7
11.0	123.0	136.5
14.2	118.7	135.5
15.9	115.4	133.7

Per: _____
